SPRINT BACKLOG

iGugulam Community Programme | Agile Portfolio of Evidence

Project started	Trello board	Sprint lists	Team
13 July 2026	PRP Agile board	1–6	Tlangelani Chauke, Lungela Nkunkuma, Templeton Dyanti

1. Project overview and team responsibilities

The Sprint Backlog documents the activities shown on the team's Trello board, including task dates, checklist progress and screenshot evidence. The board uses six sprint-labelled lists. The dates below are the card dates visible in the screenshots, not assumed formal sprint start and end dates.

Each member contributed to the frontend, backend and database components of their own assigned website features. Tlangelani Chauke additionally led and organised the Trello board. Shared research and planning cards show all three members.

2. Sprints at a glance

Sprint	Focus	Cards	Card dates (2026)
Sprint 1	Project idea and community problem	4	14–15 July
Sprint 2	Survey and research	4	14–16 July
Sprint 3	Requirements and branding	3	27–28 July
Sprint 4	User stories and interface design	3	28 July – 8 August
Sprint 5	Business and solution design	2	9–11 August
Sprint 6	Development and integration	5	17 September – 27 October

Total: 21 task cards across six sprint lists.

3. Sprint goals, task records and Trello evidence

Sprint 1 — Project idea and community problem

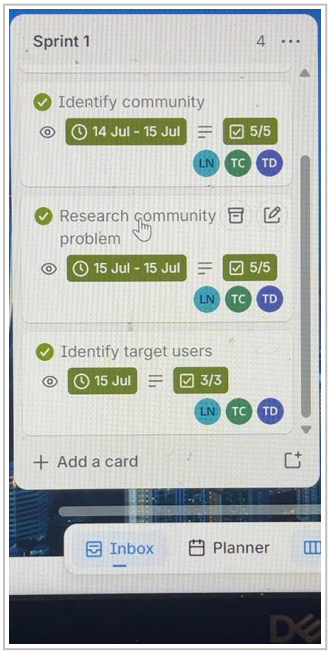


Figure 1.1: Sprint 1

Goal: Define the project idea, identify the community and research the community problem.

Trello task	Card dates (2026)	Checklist
Define project idea	14–15 July	6/6
Identify community	14–15 July	5/5
Research community problem	15 July	5/5
Identify target users	15 July	3/3

Sprint 2 — Survey and research

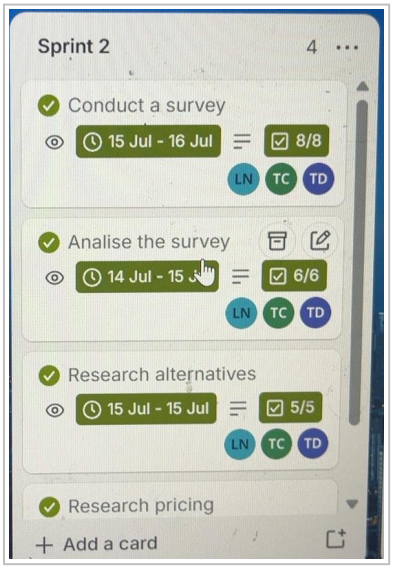


Figure 2.1: Sprint 2

Goal: Gather survey information and investigate alternatives and pricing.

Trello task	Card dates (2026)	Checklist
Conduct a survey	15–16 July	8/8
Analyse the survey	14–15 July	6/6
Research alternatives	15 July	5/5
Research pricing	16 July	5/5

Sprint 3 — Requirements and branding

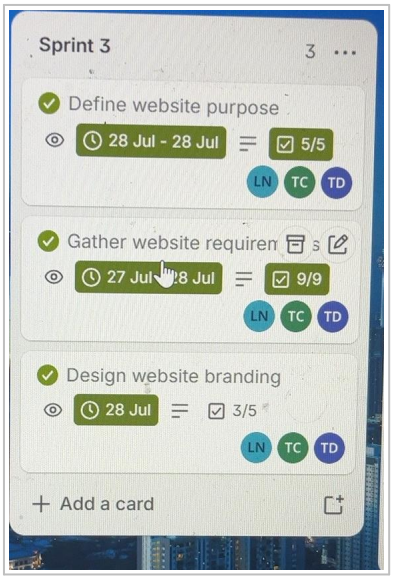


Figure 3.1: Sprint 3

Goal: Define the website purpose, gather requirements and plan branding.

Trello task	Card dates (2026)	Checklist
Define website purpose	28 July	5/5
Gather website requirements	27–28 July	9/9
Design website branding	28 July	3/5

Accuracy note: "Design website branding" has a green completed-card indicator but its checklist shows only 3/5 items checked.

Sprint 4 — User stories and interface design



Figure 4.1: Sprint 4

Goal: Develop user stories, wireframes and website UI designs.

Trello task	Card dates (2026)	Checklist
Create website user stories	6–8 August	6/6
Create website wireframes	28–31 July	6/6
Design website UI	Started 1 August	10/10

Sprint 5 — Business and solution design

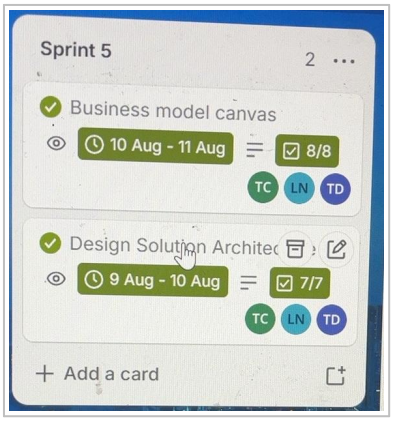


Figure 5.1: Sprint 5

Goal: Prepare the business model and solution architecture.

Trello task	Card dates (2026)	Checklist
Business model canvas	10–11 August	8/8
Design solution architecture	9–10 August	7/7

Sprint 6 — Development and integration

Goal: Develop individual features and coordinate their integration.

Trello task	Card dates (2026)	Checklist
Frontend Development (first card)	17–22 September	6/6
Frontend Development (second card)	24 September – 10 October	8/8
Backend Development	24 September – 27 October	9/9
Database Development	24 September – 27 October	9/9
System Integration	11–19 October	5/5

Accuracy note: Trello shows completed checklists; this alone does not verify that the entire integrated system was deployed or fully tested. Backend and database card date ranges extend to 27 October.

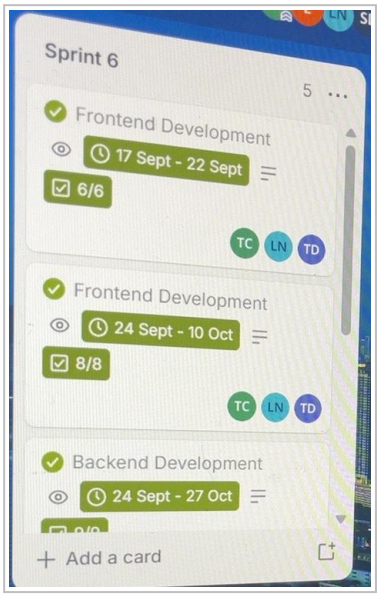


Figure 6.1: Sprint 6

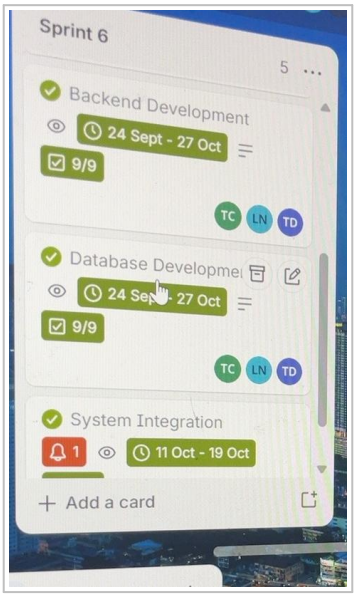


Figure 6.2: Sprint 6

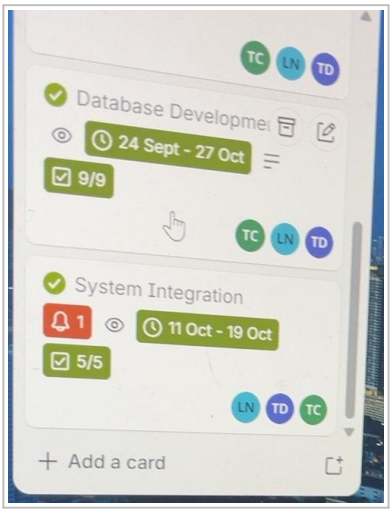


Figure 6.3: Sprint 6

4. Feature-based allocation of technical work

Member	Individual responsibilities	Shared responsibility
Tlangelani Chauke	Dashboard, Announcements, Homework and Manage Announcements; frontend, backend and database work for own features; Trello board leadership	Group planning, coordination and integration
Lungela Nkunkuma	Frontend, backend and database work for individually allocated features	Group planning, coordination and integration
Templeton Dyanti	Frontend, backend and database work for individually allocated features	Group planning, coordination and integration

5. Review of Trello evidence

The screenshots show 21 task cards across six sprint lists. The recorded checklists are fully checked for 20 cards; the website branding card shows 3/5. All three member initials (LN, TC and TD) appear on the visible sprint cards. These memberships show participation or assignment, but do not prove that each person performed every subtask.

6. Personal reflection — STAR method

Situation

Our three-member team needed to coordinate project research, website design and development for the iGugulam Community Programme. We divided technical work by feature while sharing project planning responsibilities.

Task

I was responsible for organising and leading the Trello board while developing my own assigned features: Dashboard, Announcements, Homework and Manage Announcements, including relevant frontend, backend and database work.

Action

I helped structure and monitor the tasks on Trello and followed the progress recorded in the sprint lists. I focused on my allocated features, while Lungela and Templeton worked on their separately assigned features. We coordinated on shared tasks and integration.

Result

The board provided a visible record of planned work, card dates and checklist progress. The experience strengthened my ability to coordinate tasks, take responsibility for my own development work and collaborate with other developers.

7. Lessons learned and evidence limitations

The backlog helped break a large website project into trackable tasks and showed the importance of individual accountability and team coordination. The screenshots document Trello task progress; they do not by themselves establish code quality, complete deployment or production readiness. Specific feature names for Lungela and Templeton should be added only when verified.
